TechNext

case study · construction


Every job green, red at handover.

A Singapore fit-out and M&E contractor with twelve live projects, whose margins looked healthy every month and fell away at the final account. Where the money went, and how Odoo 20 keeps it in view.

01 The problem | 02 The Odoo answer | 03 Rollout

Odoo Ready Partner | Industry case study · Construction

→ or click to begin · O all slides

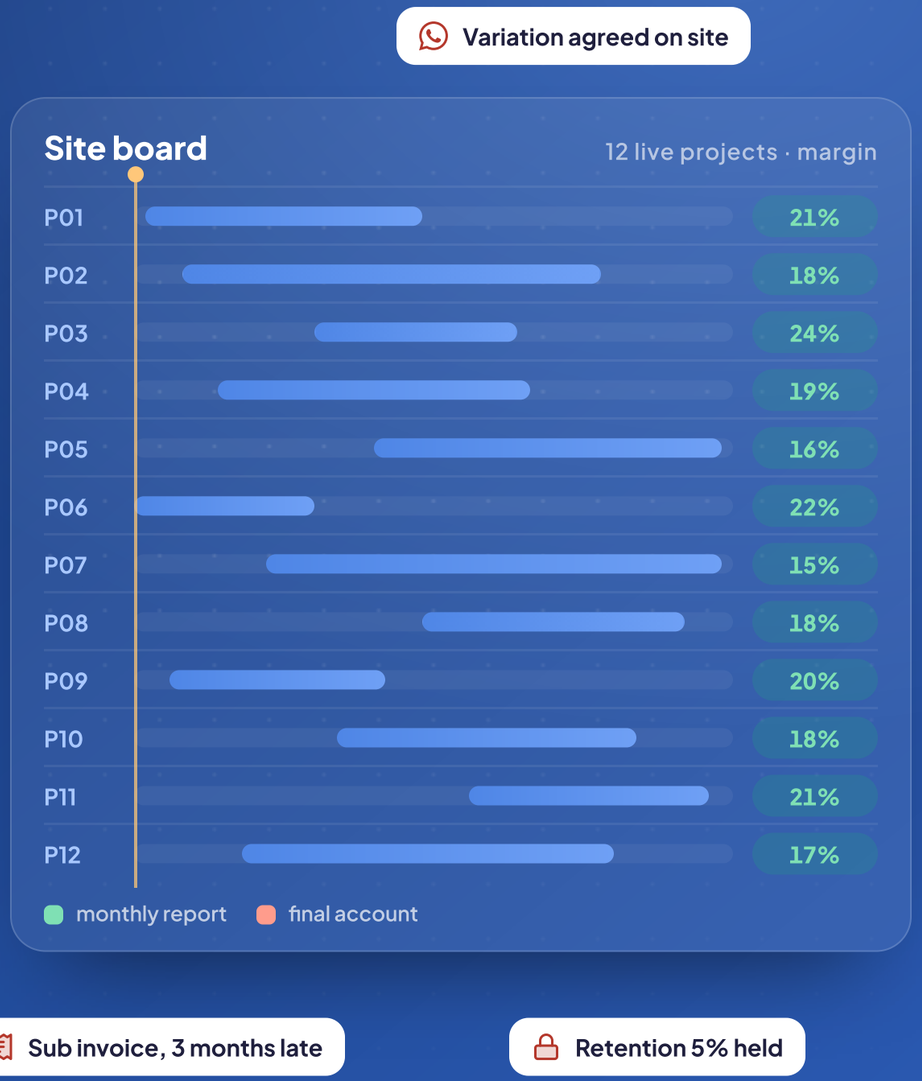

✓ Illustrative composite · sample company and figures

meet the client

Twelve jobs, all green until handover.

Monthly report | Final account

Lattwell Fit-Out

sample company · Singapore

Interior fit-out and M&E for offices, clinics, shops and hotels, mostly as a subcontractor to main contractors.

- **12** projects running at once
- **38** subcontractors
- **9** site supervisors on WhatsApp
- **7** clients claimed monthly
- **1** Excel file per progress claim

LAST YEAR'S 12 COMPLETED PROJECTS

The same jobs at the final account, after handover

P01 **12%** Clinic fit-out, Novena · S$640,000	P02 **-3%** Office, level 18, CBD · S$1,860,000	P03 **9%** Restaurant, Orchard · S$380,000	P04 **14%** Showroom, Ubi · S$520,000
P05 **4%** Office, level 6, one-north · S$1,120,000	P06 **15%** Retail unit, Jurong East · S$290,000	P07 **-1%** Hotel room refit, Bugis · S$2,400,000	P08 **6%** Lab M&E works, Science Park · S$960,000
P09 **11%** School canteen, Tampines · S$330,000	P10 **3%** Co-working floor, Tanjong Pagar · S$810,000	P11 **13%** Bank branch, Toa Payoh · S$450,000	P12 **8%** Server room M&E, Woodlands · S$700,000

Average margin **7.6%** Jobs that lost money **2**


P02 is the job we follow next

✓ Illustrative composite · sample data

the complicated part · project P02

The margin leaked a month at a time.

→ one month at a time

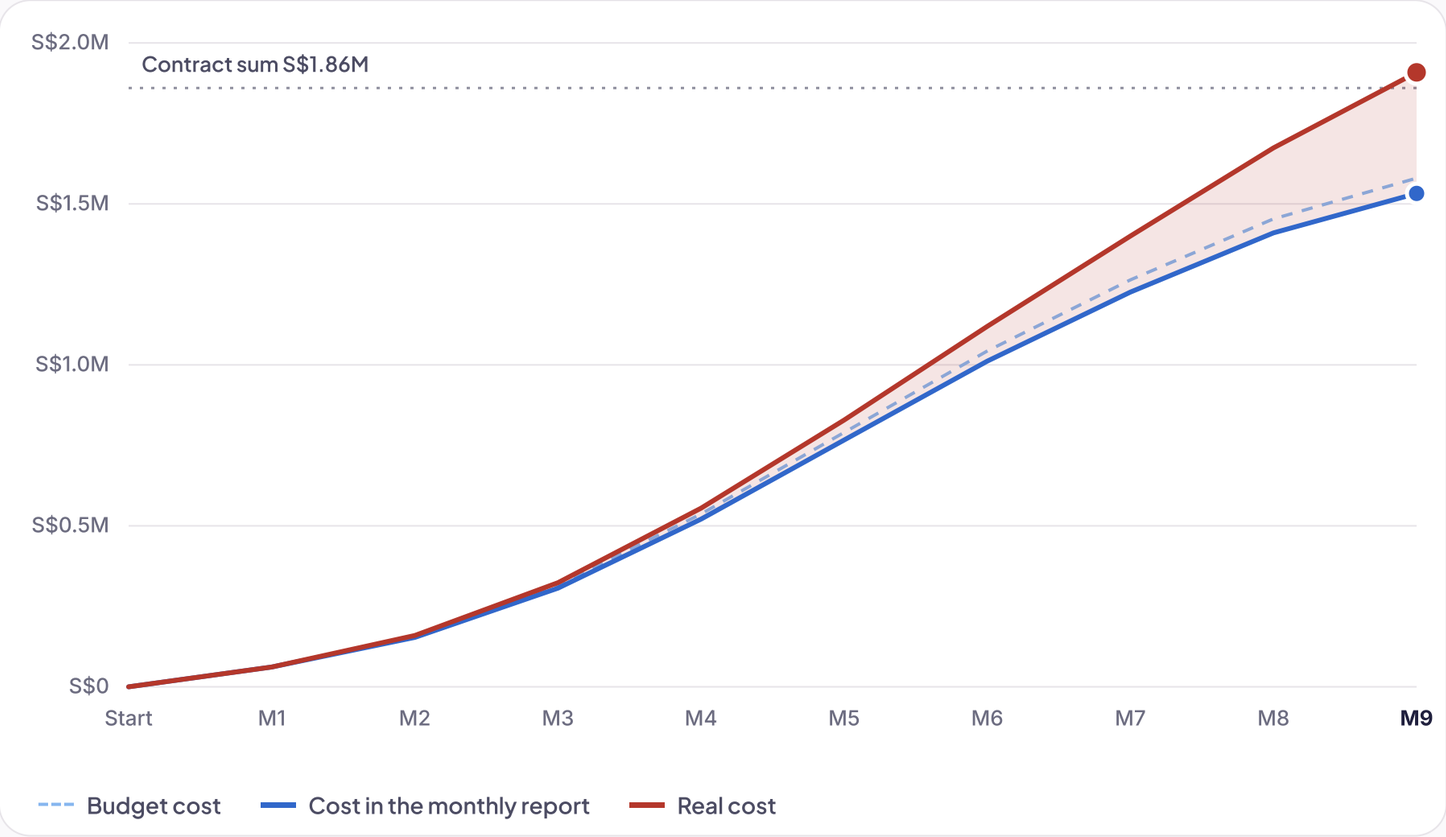

SWITCH ON WHAT THE REPORT COULD NOT SEE

- **Variations agreed on WhatsApp** — work done, never priced or claimed — **S$138,000**
- **Costs booked to other jobs** — materials moved between sites — **S$92,000**
- **Sub work not yet invoiced** — invoices arriving months late — **S$146,000**

Month 9 of 9 · handover · final account

REPORT SAYS	REAL MARGIN
17.6%	-2.6%

Retention held by the main contractor **S$93,000**, with no date to claim it back

✓ Sample figures · one project replayed

why it is hard

One month, three clocks.

- Site · every day
- Subcontractors · when they invoice
- Office · claim on the 25th

MON	TUE	WED	THU	FRI	SAT	SUN
1	2	3 VO agreed on WhatsApp	4	5	6	7
8	9 12 boards go to P05	10	11	12 Sub bills last month	13	14
15	16	17	18	19	20	21
22 QS rings: “how far?”	23	24	25 Claim 06 from Excel	26	27	28
29	30 Report says 17.6%					

MONTH 6 · P02 — Event 6 of 6

Day 30 · month-end

The cost report closes on the costs that arrived. It says 17.6%, the same as last month. Everyone moves on.

CLAIM 06, AS IT WENT OUT

WORK DONE	Guessed by phone: “about 70%”
VARIATIONS	0 of 3 included
SUB COSTS	S$58,000 not invoiced yet
RETENTION	5% held, no release date

✓ Illustrative · sample month

the odoo answer

One project, every cost in one place.

Click an app to switch it on

- **Sales** — contract lines and progress claims
- **Sales · variations** — quoted, signed online by the client
- **Purchase** — subcontracts count before the bill
- **Accounting · analytic** — every bill line tagged to a project
- **Timesheets** — own crews' hours at cost

THE SITE SIDE

- Project
- Planning · Field Service
- Documents
- Sign

Lattwell Fit-Out · Project · P02 Office, level 18

Profitability

month 7 · replayed with Odoo

Revenues	Invoiced	To invoice
Progress claims 01–07	S$1,488,000	S$0
Variation orders, signed	S$36,000	S$148,000
Costs	**Billed**	**To bill**
Subcontractors · purchase orders	S$708,000	S$104,000
Materials · vendor bills	S$364,000	S$0
Site labour · timesheets	S$226,000	S$0

MARGIN ODOO CAN SEE

16.1% all five sources, month 7

Retention receivable

S$74,400


5% of claims, on its own account


✓ Illustrative screen · sample data

workflow 1 · site to office

Agreed on site at 10 am, signed by 4 pm.

▶ Play the flow

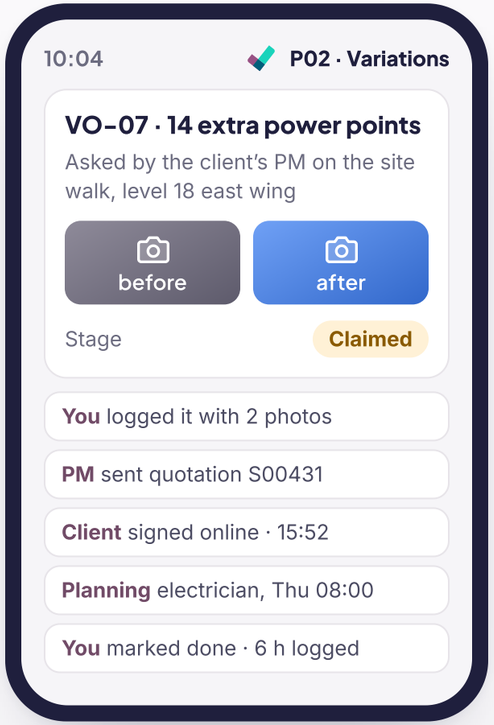

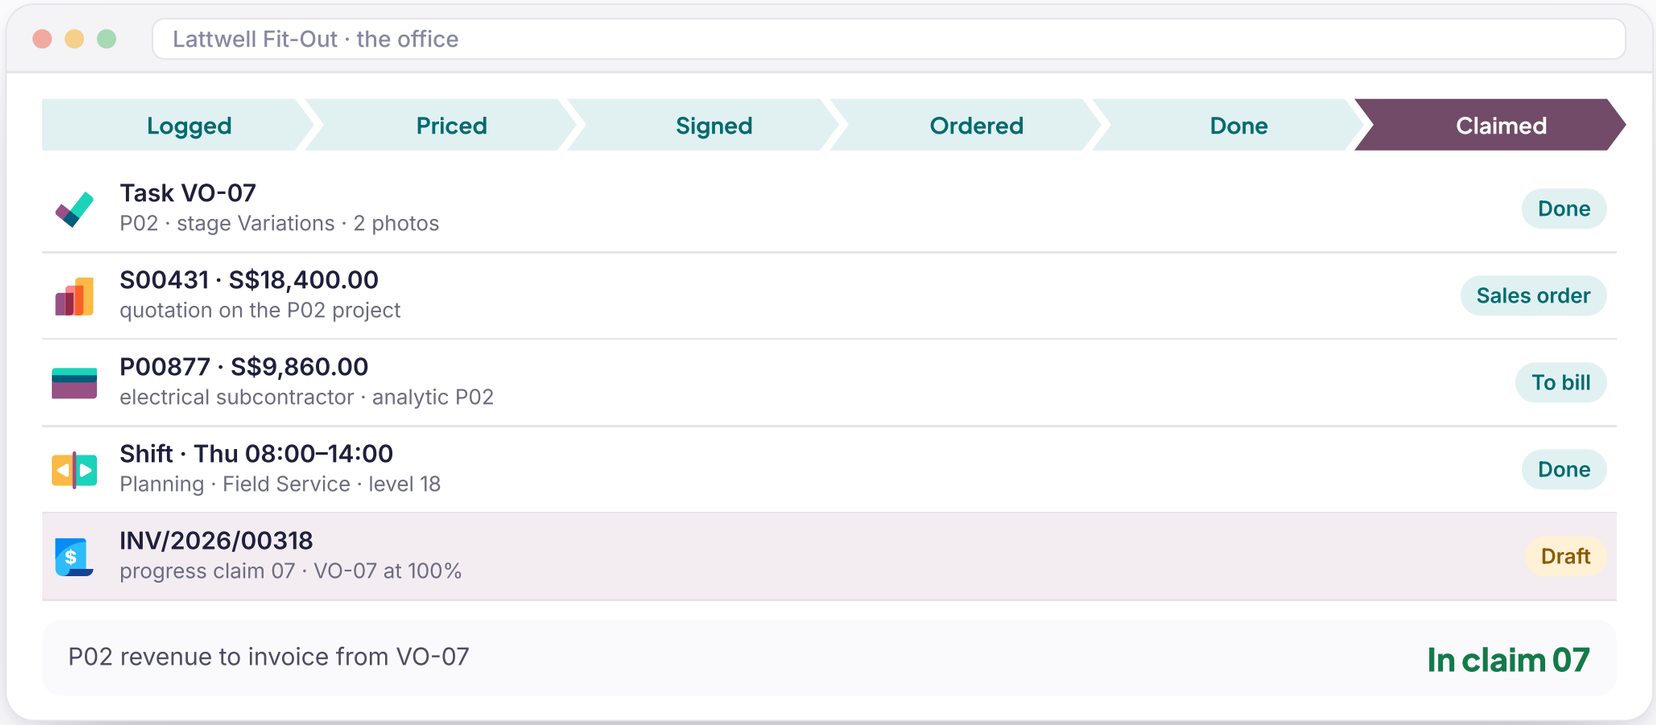

1. Supervisor logs it, with photos
2. PM prices it as a quotation
3. Client signs it online
4. Sub ordered, crew planned
5. Done: photo and hours
6. Lands in the next claim

✓ Illustrative screens · sample data

workflow 2 · the progress claim

Percent complete in, claim invoice out.

Drag any line's percent complete

Sales · S00412 · P02 Office, level 18 · claim 07

Contract line	Contract sum	Previous	Delivered to date	This claim
Partitions and doors	S$310,000	80%	95%	S$46,500.00
Ceilings	S$186,000	55%	70%	S$27,900.00
Electrical (M&E)	S$420,000	60%	72%	S$50,400.00
Air-conditioning (M&E)	S$380,000	50%	65%	S$57,000.00
Flooring	S$214,000	20%	45%	S$53,500.00
Carpentry and joinery	S$350,000	40%	55%	S$52,500.00
VO-07 · power points signed	S$18,400	0%	100%	S$18,400.00

Work done to date	S$1,281,300.00
Less previous claims	-S$975,100.00
This claim	S$306,200.00
Less retention 5%	-S$15,310.00
Amount due before GST	**S$290,890.00**

Create Invoice

INV/2026/00318 Draft

Claim 07 · 7 lines	S$306,200.00
Retention 5% · own account	-S$15,310.00
Total before GST	**S$290,890.00**

✓ Illustrative screen · sample contract

how we rolled it out

Two live jobs first, then all twelve.

1 Foundation
Accounting · Purchase

2 Two pilot jobs
Project · Sales · Purchase

3 Site on phones
Planning · Timesheets · Sign

4 All twelve jobs
Budgets · dashboards

WE DO

One analytic plan for projects, cost codes per trade, a budget per job, the retention account, and analytic made mandatory on every purchase and bill line.

- Accounting · analytic plans
- Purchase
- Budgets per project

~~Materials bought "for the company"~~ → Every line bought for a project

~~Retention in someone's memory~~ → Retention on its own account

Run a fit-out or M&E firm?

30-minute call with an adviser · online

+65 8839 6998
sales@technext.asia

✓ Illustrative composite · no client figures
